


ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	March 2024					
							18	21	24	27	1	4
1		PRECONSTRUCTION MEETING	1 day	Tue 2/27/24	Tue 2/27/24							
2		SITE CLEARING	5 days	Wed 2/28/24	Tue 3/5/24	1						
3		REMOVALS	2 days	Wed 2/28/24	Thu 2/29/24	2SS						
4		EROSION CONTROL INSTALLATION/CONS ENTRANCE	1 day	Wed 2/28/24	Wed 2/28/24	1						
5		36" PIPE	16 days	Tue 3/5/24	Tue 3/26/24	3						
6		MANHOLES	5 days	Tue 3/5/24	Mon 3/11/24	5SS						
7		MAIN STREET CLOSURE	10 days	Mon 3/11/24	Fri 3/22/24	5						
8		UTILITY POTHOLING	1 day	Mon 3/11/24	Mon 3/11/24	7SS						
9		PATCHING OF MAIN STREET (PCCP 12")	6 days	Fri 3/15/24	Fri 3/22/24	7FF						
10		TIE INTO EXISTING STRUCTURES	2 days	Mon 3/25/24	Tue 3/26/24	9						
11		24" PIPE	2 days	Wed 3/27/24	Thu 3/28/24	10						
12		18" PIPE	2 days	Fri 3/29/24	Mon 4/1/24	11						
13		12" PIPE	2 days	Tue 4/2/24	Wed 4/3/24	12						
14		8" PIPE	6 days	Thu 4/4/24	Thu 4/11/24	13						
15		YARD DRAINS	3 days	Tue 4/9/24	Thu 4/11/24	14FF						
16		RETAINING WALLS	7 days	Fri 4/12/24	Mon 4/22/24	15						
17		RESTORATION	2 days	Fri 4/19/24	Mon 4/22/24	16FF						



Project: Elm Street Drain Pendle
Date: Tue 2/27/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

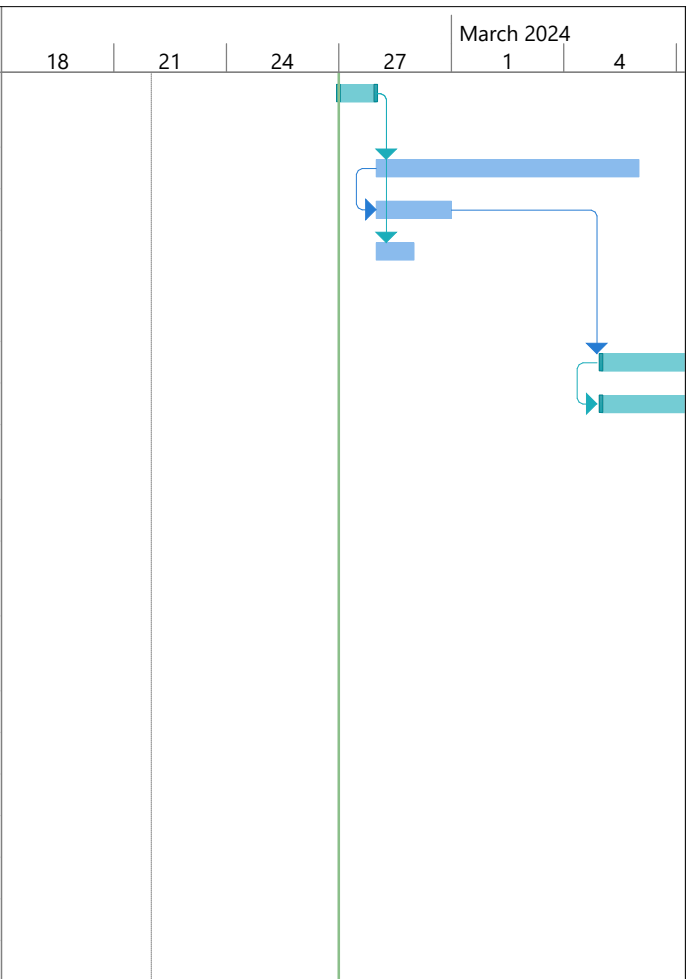
